

WORKSHEET
Restoration of Koehl Lot
Section D, Lot 162 W 1/2

May 31, 2005

Employee	Hours	Rate	\$
Rodriguez, Mario	5	25.00	125.00
Aguilar, Teofilo	5	15.00	75.00
TOTAL LABOR			200.00
Equipment	Hours	Hourly Rate	\$
Yellow Tractor	3	12.50	37.50
Pressure Washer	1	10.00	10.00
TOTAL EQUIPMENT			47.50
Materials	Quantity	Unit Price	\$
Ready-mixed concrete (80# bag)	11	2.45	26.95
Sod - St. Augustine (s.f.)	3	0.31	0.93
TOTAL MATERIALS			27.88
TOTAL LABOR, EQUIPMENT, MATERIALS			275.38
		Plus 11 percent	30.29
		GRAND TOTAL	305.67

TIME SHEET

GLENWOOD CEMETERY

PROJECT KOEHL EST Ave:

5 - 31, 2005

Employee	In	Out	Hours Worked	Worked Performed
Mario Rodriguez	7:Am.	12: Pm.	5	
Ramon Estrada				
Teofilo Aguilar	7:Am.	12: Pm.	5	
TOTAL HOURS				

Equipment Used	Hours Used	Worked Performed
yellow TRACTOR	3.	

Materials Used	Quantity Used
11 Bagg concrete mix	
80 pound.	

Compiled by _____, _____, 2005
Martha W. Peterson

Approved by _____, _____, 2005
Richard A. Ambrus

GLENWOOD CEMETERY

To: Dick Ambrus
From: Martha Peterson
Subject: Monument Restoration – Koehl (D-162 W½)
Date: June 2, 2005

Attached is a “before and after” of a monument in the north part of Section D. I plan to retake the “after” photo because it doesn’t look plumb.

Before work began on this monument, the epitaph faced west. It was put back together with the epitaph facing east. Mario says he can turn it. Is it worth the expense? Note that the last burial was in 1894.

MP

Attachment


*Leave it as is
per RAA
6-2-05.
mp*

MONUMENT RESTORATION PROJECT

Section Lot No. Description	D 162 W½	Lot Owner Purchase Date Deed of Perpetuity Contact Last Burial	M. J. Koehl 1885 No None 1894	
Work Performed	A 67" tall marble monument was almost plumb, but had no foundation. It was sitting atop concrete pavers, leveled by small stones used as shims (see photograph below). The finial had broken off and was lying on the ground. The monument is inscribed with the manufacturer's name, Seager & Co., of Houston.			
Cost	\$295.00, including labor, equipment and materials.			



Before: The monument is almost plumb, but is not on a proper foundation. It is sitting on concrete pavers, leveled by small stones used as shims.

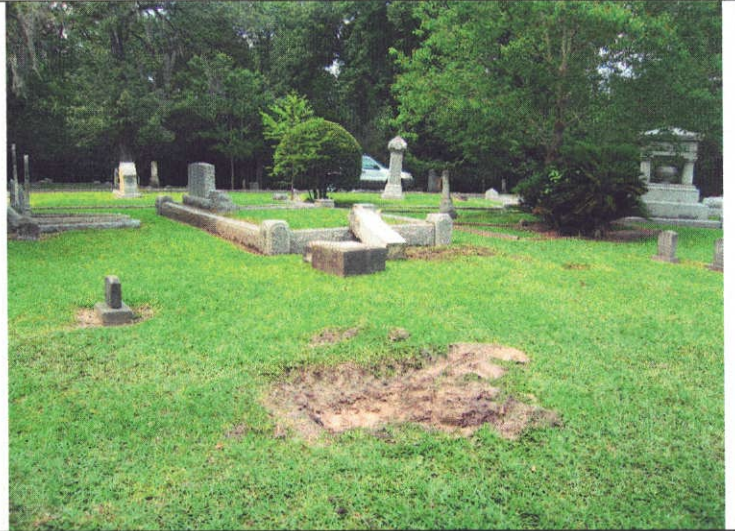

Before: Excavation reveals no foundation under the monument.



The Koehl monument is one of relatively few in Glenwood that identify the manufacturer.



After: The monument has been leveled and reset on a proper foundation. The sod around the base of the monument will be replaced.
