


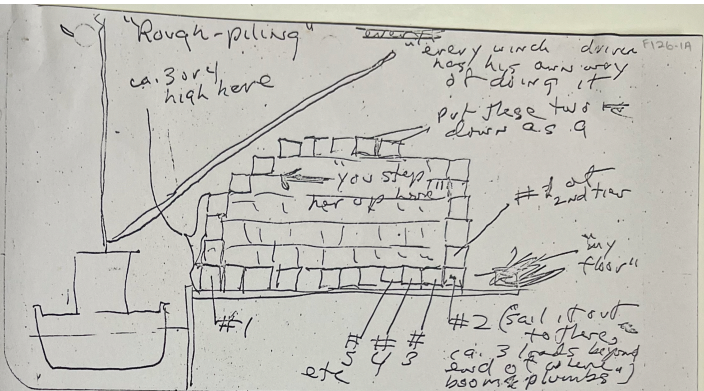

HAYSTACKING

1. Start here - (on dock near ship side) with 2 sling loads to form kind of a bulkhead.
2. Then sling loads are topples over behind the "bulkhead formed by the first two loads.

When lumber is picked up again it has to be piece by piece.

ROUGH PILING

You keep the load together so it can be picked up again. This is a all a matter of the way the sling is drawn out when the load is set d down.

Land the first load about 3 loads beyond where the boom plumbs.
"Sail it out to there".

Then land the next load next to the first but nearer to the ship.

At the under the boom Bank high you'll have to start stepping

After the loads get 3 or 4 high you have to start stepping them up under the slope of the boom.

"every winchdriver had his own way of doing it."

Nick Olsen: San Pedro, 11/12/63

